


ID	Task Mode	Task Name	Prime	% Complete	Duration	Start	Finish	Predecessors	Material Delivery	August	September	October	November	December	January	February	March	April	May	June	July
1	✓	Trailers, Connex and Temp Parking	LCS	100%	1 day	Fri 9/1/23	Fri 9/1/23														
2	✓	Temp Power	USC	100%	1 day	Fri 9/1/23	Fri 9/1/23														
3		LeChase Mobilization	LCS	0%	1 day	Wed 9/13/23	Wed 9/13/23														
4		Temp Fence	LCS	0%	2 days	Thu 9/14/23	Fri 9/15/23	3													
5		Concrete Demo and Slab on Grade Rough Grade	LCS	0%	10 days	Thu 9/14/23	Wed 9/27/23	3													
6		Footer and Foundation Prep	LCS	0%	5 days	Thu 9/28/23	Wed 10/4/23	5													
7		Footer and Foundation FRP	LCS	0%	30 days	Thu 10/5/23	Wed 11/15/23	6													
8		Foundation Insulation and Waterproofing	LCS	0%	5 days	Thu 11/16/23	Wed 11/22/23	7													
9		Stem Wall Sealing	LCS	0%	2 days	Thu 11/16/23	Fri 11/17/23	7													
10		Under Slab Masonry	LCS	0%	10 days	Thu 11/23/23	Wed 12/6/23	8													
11		Backfill and Footer Drain	LCS	0%	10 days	Thu 12/7/23	Wed 12/20/23	8,10													
12		Plumbing Storm Piping Exterior	SLV	0%	10 days	Thu 12/14/23	Wed 12/27/23	11FS-5 days													
13		Plumbing Sanitary Undreground Office Area	SLV	0%	5 days	Thu 11/23/23	Wed 11/29/23	8													
14		Plumbing Sanitary Undreground Main Garage	SLV	0%	10 days	Thu 11/23/23	Wed 12/6/23	8													
15		Slab on Grade Prep	LCS	0%	5 days	Thu 12/7/23	Wed 12/13/23	14													
16		Install Vapor Barrier and Insulation	LCS	0%	3 days	Thu 12/14/23	Mon 12/18/23	15													
17		Plumbing Install Trench Drains	SLV	0%	8 days	Tue 12/19/23	Thu 12/28/23	16													
18		Elec In Slab Rough Ins	USC	0%	10 days	Tue 12/19/23	Mon 1/1/24	16													
19		Install Radiant Floor Tubing	J&K	0%	5 days	Wed 1/10/24	Tue 1/16/24	24FF													
20		Slab on Grade FRP w/ Embeds	LCS	0%	10 days	Thu 1/11/24	Wed 1/24/24	17,16,18,19													
21		Water Main Infastructure	LCS	0%	7 days	Thu 10/5/23	Fri 10/13/23	6													
22		Site Electric Excavation	LCS	0%	2 days	Mon 10/16/23	Tue 10/17/23	21													
23		Site Electric Utilities (Transformer Vault/Elec	USC	0%	5 days	Wed 10/18/23	Tue 10/24/23	22													
24		Storm Infastructure	LCS	0%	4 days	Wed 10/18/23	Mon 10/23/23	22													
25		Sanitary Infastructure	LCS	0%	4 days	Tue 10/24/23	Fri 10/27/23	24													
26		Generator Pad FRP	USC	0%	2 days	Thu 10/26/23	Fri 10/27/23	23													
27	👤	Generator Install	USC	0%	4 days	Thu 2/1/24	Tue 2/6/24		Need Delivery Date												
28		Heat Pump Pad FRP	J&K	0%	2 days	Thu 10/26/23	Fri 10/27/23	26SS													
29	👤	Heat Pump Unit Install	J&K	0%	5 days	Thu 2/1/24	Wed 2/7/24		Need Delivery Date												
30		Apron Prep w/ Ext Bollards	LCS	0%	10 days	Thu 12/21/23	Wed 1/3/24	11													
31		Aprons FRP w/ Exterior Bollards	LCS	0%	15 days	Thu 1/4/24	Wed 1/24/24	30													
32		PEMP Building Frame, Roof Panels and Wall Panels	LCS	0%	40 days	Mon 12/4/23	Fri 1/26/24		Delivery the week before 12/4												

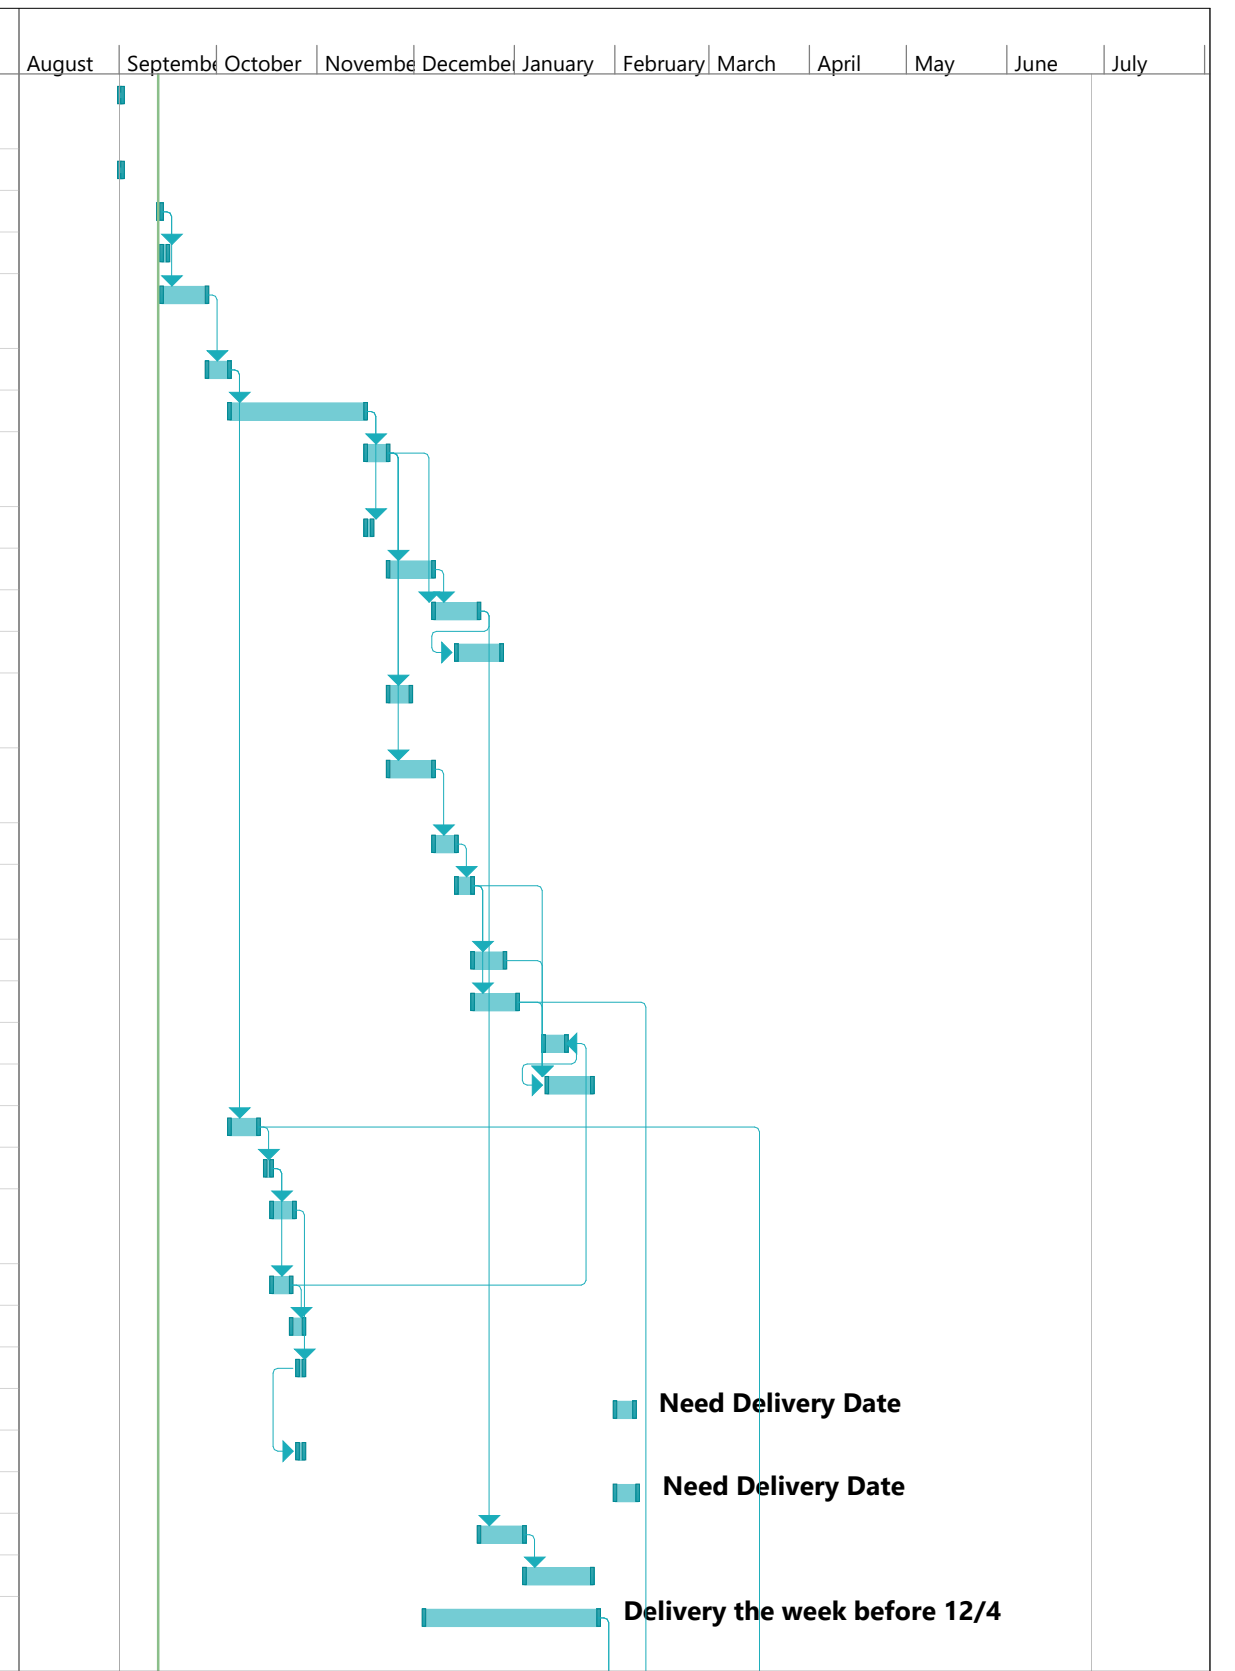

Project: Windsor Project Schedule
Date: Wed 9/13/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Prime	% Complete	Duration	Start	Finish	Predecessors	Material Delivery	August	September	October	November	December	January	February	March	April	May	June	July
33	➤	Temp Weather Protections	LCS	0%	10 days	Mon 1/29/24	Fri 2/9/24	32													
34	➤	Door Frames Masonry	LCS	0%	5 days	Mon 1/29/24	Fri 2/2/24	32													
35	➤	Office Masonry w/ Insulation	LCS	0%	10 days	Mon 2/12/24	Fri 2/23/24	33,34													
36	➤	Elec Masonry Rough Ins	USC	0%	15 days	Mon 2/12/24	Fri 3/1/24	18,35SS													
37	➤	Main Garage Masonry w/ Insulation	LCS	0%	10 days	Mon 2/19/24	Fri 3/1/24	35SS+5 days													
38	➤	Overhead Door Install	LCS	0%	10 days	Mon 3/4/24	Fri 3/15/24	37													
39	➤	Ext Man Door Install	LCS	0%	10 days	Mon 3/4/24	Fri 3/15/24	35,37													
40	➤	Ext/Int Window Install	LCS	0%	20 days	Mon 3/4/24	Fri 3/29/24	35,37													
41	➤	Mezzanine Steel Install	LCS	0%	10 days	Mon 2/26/24	Fri 3/8/24	35													
42	➤	Slab on Metal Deck FRP	LCS	0%	5 days	Mon 3/11/24	Fri 3/15/24	41													
43	➤	Install Fans (Exhaust Fans and Vehicle Exhaust Fans)	J&K	0%	15 days	Mon 3/18/24	Fri 4/5/24	42													
44	➤	Vehicle Exhaust System	J&K	0%	10 days	Mon 4/8/24	Fri 4/19/24	43													
45	➤	Office Area Framing	LCS	0%	5 days	Mon 3/11/24	Fri 3/15/24	41													
46	➤	Plumbing In Wall Rough In Office Area	SLV	0%	12 days	Mon 3/18/24	Tue 4/2/24	45,35													
47	➤	Plumbing Above Ceiling Rough In Office Area	SLV	0%	8 days	Wed 4/3/24	Fri 4/12/24	35,45,46													
48	➤	Plumbing Water Room	SLV	0%	7 days	Mon 3/18/24	Tue 3/26/24	21,45													
49	➤	Plumbing Rough In Above Slab Main Garage	SLV	0%	20 days	Mon 3/4/24	Fri 3/29/24	37													
50	➤	Fire Alarm Rough Ins	USC	0%	8 days	Mon 3/18/24	Wed 3/27/24	45													
51	➤	Elec Light and Power Rough Ins	USC	0%	25 days	Mon 3/18/24	Fri 4/19/24	45													
52	➤	Elec Wire Installation	USC	0%	10 days	Mon 4/22/24	Fri 5/3/24	51													
53	➤	Install Duct Work and Accessor	J&K	0%	25 days	Mon 3/18/24	Fri 4/19/24	45													
54	➤	Refrigeration Piping	J&K	0%	5 days	Mon 4/22/24	Fri 4/26/24	53													
55	➤	Office Area Drywall	LCS	0%	10 days	Mon 3/18/24	Fri 3/29/24	45													
56	➤	Office Area Door Frames	LCS	0%	5 days	Mon 4/1/24	Fri 4/5/24	55													
57	➤	MDP and Panelboard Install	USC	0%	5 days	Mon 4/1/24	Fri 4/5/24	55	Need Date												
58	➤	Install Electric Heater/Unit Heaters	J&K	0%	5 days	Mon 4/1/24	Fri 4/5/24	55													
59	➤	Stair and Railing Install	LCS	0%	10 days	Mon 4/8/24	Fri 4/19/24	45,55,56													
60	➤	Bridge Crane Install	LCS	0%	5 days	Mon 1/22/24	Fri 1/26/24		Delivery the week before 1/22												
61	➤	Finished and Paint	LCS	0%	15 days	Mon 3/25/24	Fri 4/12/24	55FS-5 days													
62	➤	Plumbing Fixtures and Trim Office Area	SLV	0%	3 days	Mon 4/15/24	Wed 4/17/24	61													
63	➤	Fire Alarm Device Install	USC	0%	10 days	Mon 4/15/24	Fri 4/26/24	61,50													


Need Date

Delivery the week before 1/22

Project: Windsor Project Schedu
Date: Wed 9/13/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Prime	% Complete	Duration	Start	Finish	Predecessors	Material Delivery	August	September	October	November	December	January	February	March	April	May	June	July
64	➤	Elec Device Installation (Switched and Recep)	USC	0%	7 days	Mon 4/15/24	Tue 4/23/24	61													
65	➤	Elec Final Trim Out	USC	0%	5 days	Wed 4/24/24	Tue 4/30/24	64													
66	➤	Owner Equipment Set	Windsor	0%	5 days	Thu 4/18/24	Wed 4/24/24	67SF	Communicate to owner.												
67	➤	Plumbing Fixtures and Trim Main Garage	SLV	0%	10 days	Thu 4/18/24	Wed 5/1/24	62													
68	➤	Install Radiant Heater System	J&K	0%	12 days	Mon 4/22/24	Tue 5/7/24	44													
69	➤	Install Propane Piping for Radiant Heater System	J&K	0%	7 days	Wed 5/8/24	Thu 5/16/24	68													
70	➤	Controls and Wiring	J&K	0%	15 days	Fri 5/17/24	Thu 6/6/24	69													
71	➤	Insulation	J&K	0%	3 days	Fri 6/7/24	Tue 6/11/24	70													
72	➤	Install RGD's	J&K	0%	2 days	Wed 6/12/24	Thu 6/13/24	71													
73	➤	HVAC Final Connections	USC	0%	8 days	Wed 6/12/24	Fri 6/21/24	71													
74	➤	Heat Pump Start-up and Owner Instruction	J&K	0%	3 days	Mon 6/24/24	Wed 6/26/24	73													
75	➤	Interior Doors	LCS	0%	5 days	Mon 4/8/24	Fri 4/12/24	61FS-5 days													
76	➤	Door Hardware	LCS	0%	5 days	Mon 3/18/24	Fri 3/22/24	39,75													
77	➤	Fire Sprinkler Rough In Office Area	SLV	0%	10 days	Mon 4/22/24	Fri 5/3/24	53													
78	➤	Fire Sprinkler Rough In Main Garage	SLV	0%	10 days	Mon 4/22/24	Fri 5/3/24	53													
79	➤	Ceiling Grid and Install	LCS	0%	10 days	Mon 4/15/24	Fri 4/26/24	61													
80	➤	Lighting Installation	USC	0%	10 days	Mon 4/29/24	Fri 5/10/24	51,79													
81	➤	Fire Sprinkler Heads/Trim	SLV	0%	5 days	Mon 4/29/24	Fri 5/3/24	79													
82	➤	Flooring Install	LCS	0%	10 days	Mon 4/29/24	Fri 5/10/24	79													
83	➤	Sign Install	LCS	0%	10 days	Mon 5/13/24	Fri 5/24/24	82													
84	➤	Accessories Install	LCS	0%	5 days	Mon 5/13/24	Fri 5/17/24	82													
85	➤	Millwork Install	LCS	0%	10 days	Mon 5/13/24	Fri 5/24/24	82													
86	➤	Final Cleaning	LCS	0%	5 days	Mon 5/27/24	Fri 5/31/24	83,84,85													
87	➤	Air Balance Work	J&K	0%	5 days	Mon 6/3/24	Fri 6/7/24	86													
88	➤	Furniture Install	LCS	0%	5 days	Mon 6/3/24	Fri 6/7/24	86													
89	➤	Top Soil and Seeing	LCS	0%	5 days	Mon 4/22/24	Mon 4/29/24	90SF													
90	➤	Asphalt Final Grade	LCS	0%	5 days	Mon 4/29/24	Fri 5/3/24		Start 4/29												
91	➤	Asphalt (Binder and Top)	LCS	0%	10 days	Mon 5/6/24	Fri 5/17/24	90													
92	➤	Pavemet Striping	LCS	0%	5 days	Mon 5/20/24	Fri 5/24/24	91													

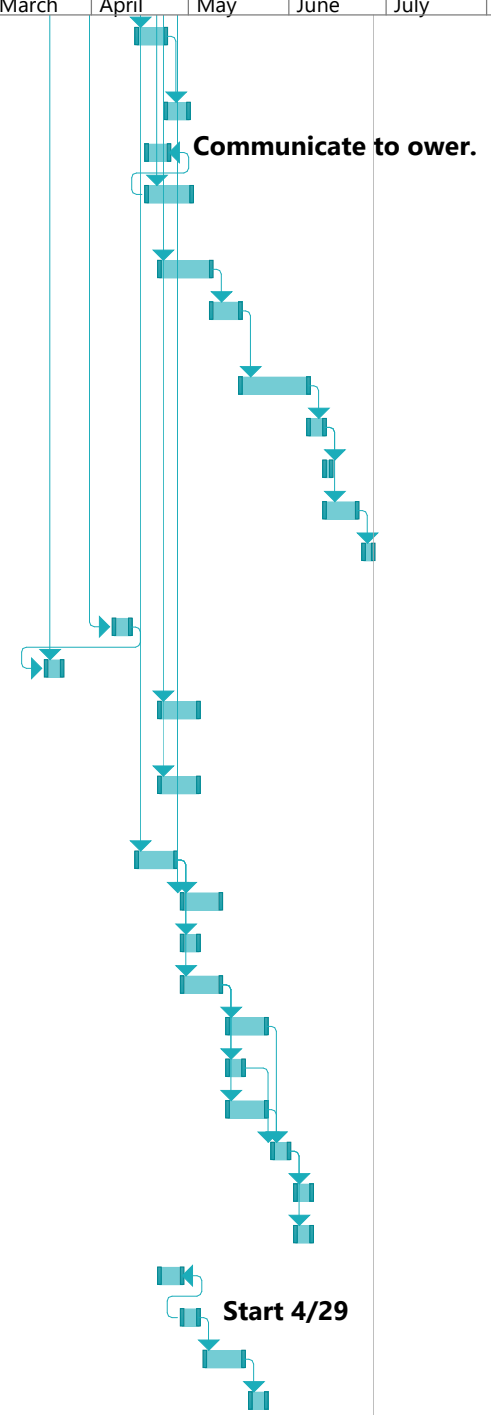

Project: Windsor Project Schedule Date: Wed 9/13/23	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
